





# CITY OF BETHANY

## OKLAHOMA

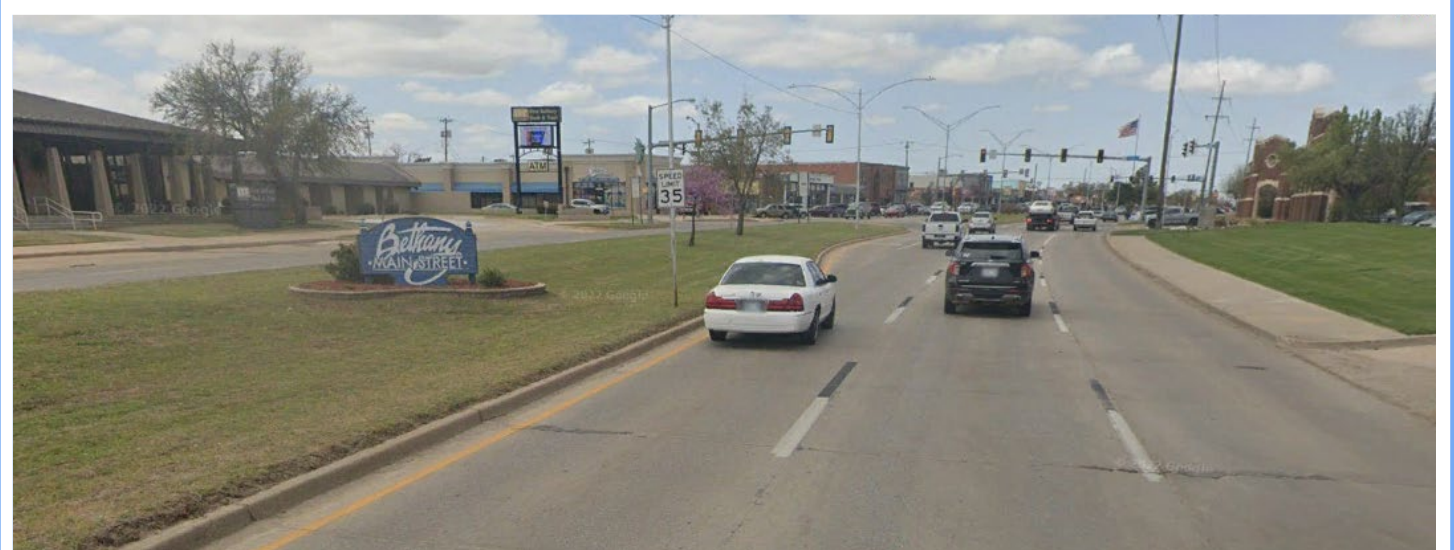

G.O. BOND / ARPA FUNDED PROJECT UPDATES  
ODOT SH-66 PROPOSED IMPROVEMENTS



# PROPOSITION 1-A

## NW 23<sup>RD</sup> STREET / ROCKWELL

CITY OF BETHANY



### Traffic Signalization and Pedestrian Crosswalk Improvements

This project will also include the CRRSAA mill and inlay of the intersection, extending north approximately 1,000 feet.

- Survey complete
- Traffic signal under design - TEC
- Roadway mill & inlay under design
- CRRSAA project agreement with ODOT approved at June 13<sup>th</sup> City Council Meeting
- Anticipated let date for signals: Fall 2023
- Anticipated let date for CRRSAA mill and inlay – Late 2024

# PROPOSITION 1-B

## NW 36<sup>TH</sup> / ROCKWELL

CITY OF BETHANY



## Traffic Signalization and Pedestrian Crosswalk Improvements

- Survey complete
- Traffic signal under design - TEC
- Anticipated let date – Winter 2023



# PROPOSITION 1-C


## NW 36<sup>TH</sup> / COUNCIL ROAD

CITY OF BETHANY



## Traffic Signalization and Pedestrian Crosswalk Improvements

- Survey underway
- Evaluating additional funding sources for corridor improvements

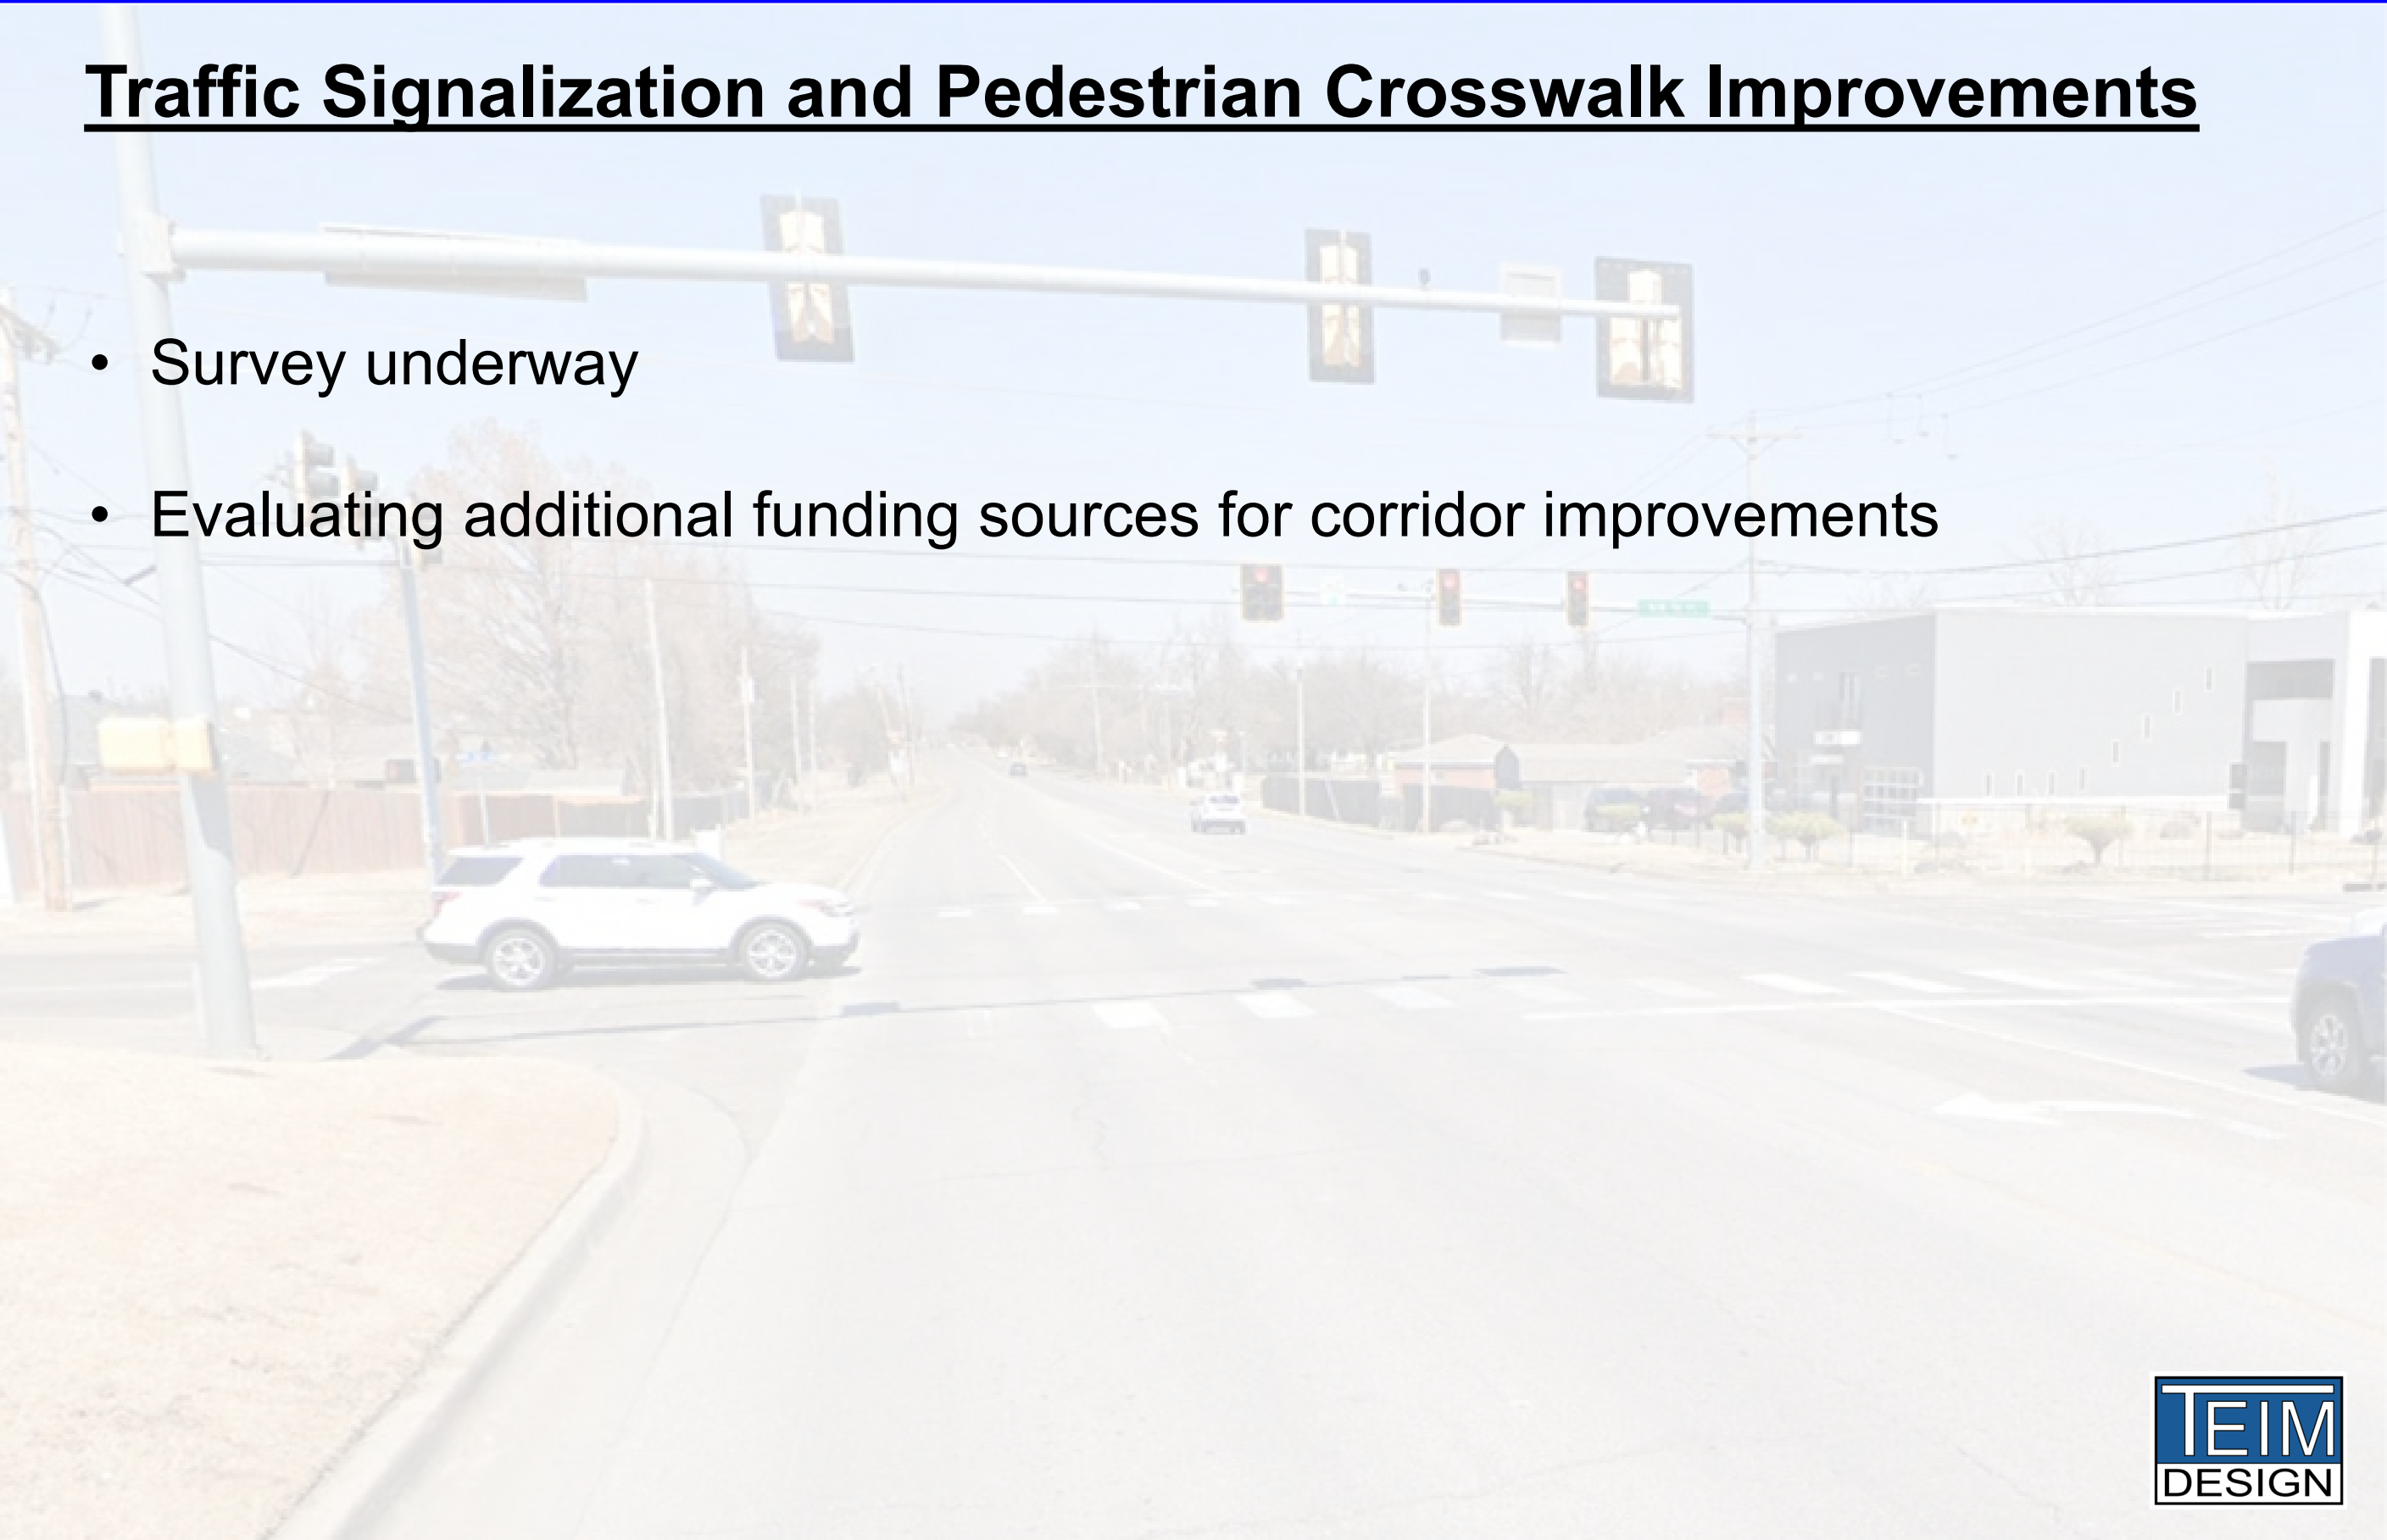

# PROPOSITION 1-D

## PENIEL – 39<sup>TH</sup> TO 42<sup>ND</sup>

CITY OF BETHANY



### **Peniel Ave. from NW 39<sup>th</sup> Expressway to NW 42<sup>nd</sup> Street**

Reconstruction of Peniel Avenue beginning at NW 39<sup>th</sup> Expressway extending north approximately 1,300 feet to NW 42<sup>nd</sup> Street. Reconstruction of Plain Jointed PC Concrete.

Survey: Complete

Environmental: Complete

Roadway Design: 65% Complete. Plan in hand scheduled July 11, 2023

Anticipated Let date: TBD due to possible conflicts with sanitary sewer replacement. Sewer line video underway.

# PROPOSITION 1-E

## NW 30<sup>TH</sup> – ROCKWELL TO PENIEL

CITY OF BETHANY



### NW 30<sup>th</sup> Street from Rockwell Avenue to Peniel Avenue

Reconstruction of NW 30<sup>th</sup> pavement beginning at Rockwell Avenue extending east approximately 2,600 feet to Peniel Avenue. Reconstruction of Plain Jointed PC Concrete.

Survey: Complete

Environmental: Complete

Roadway Design: 65% Complete. Plan in hand scheduled July 11, 2023

Anticipated Let Date: Fall 2023

# PROPOSITION 1-F

## MUELLER – NW 44<sup>TH</sup> TO NW 50<sup>TH</sup>

CITY OF BETHANY



### N. Mueller Avenue from NW 44<sup>th</sup> Street to NW 50<sup>th</sup> Street


Reconstruction of Mueller Avenue pavement beginning at NW 44<sup>th</sup> Street extending north approximately 1,960 feet to NW 50<sup>th</sup> Street.  
Reconstruction of Plain Jointed PC Concrete.

Survey: Complete

Environmental: Complete

Roadway Design: 65% Complete. Plan in hand scheduled July 11, 2023

Anticipated Let Date: Fall 2023



# PROPOSITION 1-G

## DIVIS – NW 36<sup>TH</sup> TO NW 39<sup>TH</sup>

CITY OF BETHANY



### N. Divis Avenue from NW 36<sup>th</sup> Street to NW 39<sup>th</sup> Expressway

Reconstruction of the west half of Divis Street beginning at NW 36<sup>th</sup> Street extending north approximately 1,960 feet to just south of NW 39<sup>th</sup> Expressway. Reconstruction of Plain Jointed PC Concrete.

Survey: Complete

Environmental: Complete

Roadway Design: 65% Complete. Plan in hand scheduled July 11, 2023

Anticipated Let Date: Fall 2023

# PROPOSITION 1-H

## PENIEL – NW 25<sup>TH</sup> TO NW 30<sup>TH</sup>

CITY OF BETHANY



### Peniel Avenue from NW 25<sup>th</sup> Street to NW 30<sup>th</sup> Street

Reconstruction of the west half of Peniel Avenue beginning at NW 25<sup>th</sup> Street extending north approximately 1,955 feet to NW 30<sup>th</sup> Street. Reconstruction of Plain Jointed PC Concrete.

Survey: Complete

Environmental: Complete

Roadway Design: 65% Complete. Plan in hand scheduled July 11, 2023

Anticipated Let Date: TBD due to possible conflicts with sanitary sewer replacement. Sewer line video underway.

# PROPOSITION 2-A ELDON LYON PARK

CITY OF BETHANY



## Repair, improve, remodel, equip, and renovate playground, exercise station, multipurpose shelters, and remodel restroom facilities.

- Restroom facilities have been inspected and evaluated for remodel.
- Multipurpose shelter concepts presented and recommended for approval by the Parks Board.
- Final scope approved - design process being finalized.

# PROPOSITION 2-B

## RIPPER PARK

CITY OF BETHANY



### Acquiring and improving playground equipment, and constructing or remodeling restroom facilities

- Restroom facilities have been inspected and evaluated for remodel
- Final scope approved – design process being finalized.

# PROPOSITION 2-C

## HENRY GARRISON PARK

CITY OF BETHANY



### Acquiring and improving playground equipment, constructing a multipurpose pavilion, and constructing or remodeling restroom facilities

- Restroom facilities have been inspected and evaluated for remodel
- Multipurpose shelter concepts presented and recommended for approval by the Parks Board
- Final scope approved – design process being finalized.

# PROPOSITION 2-D


## MACRORY PARK

CITY OF BETHANY



### Acquiring and improving playground equipment, and constructing or remodeling restroom facilities

- Restroom facilities have been inspected and evaluated for remodel
- Final scope approved – design process being finalized.

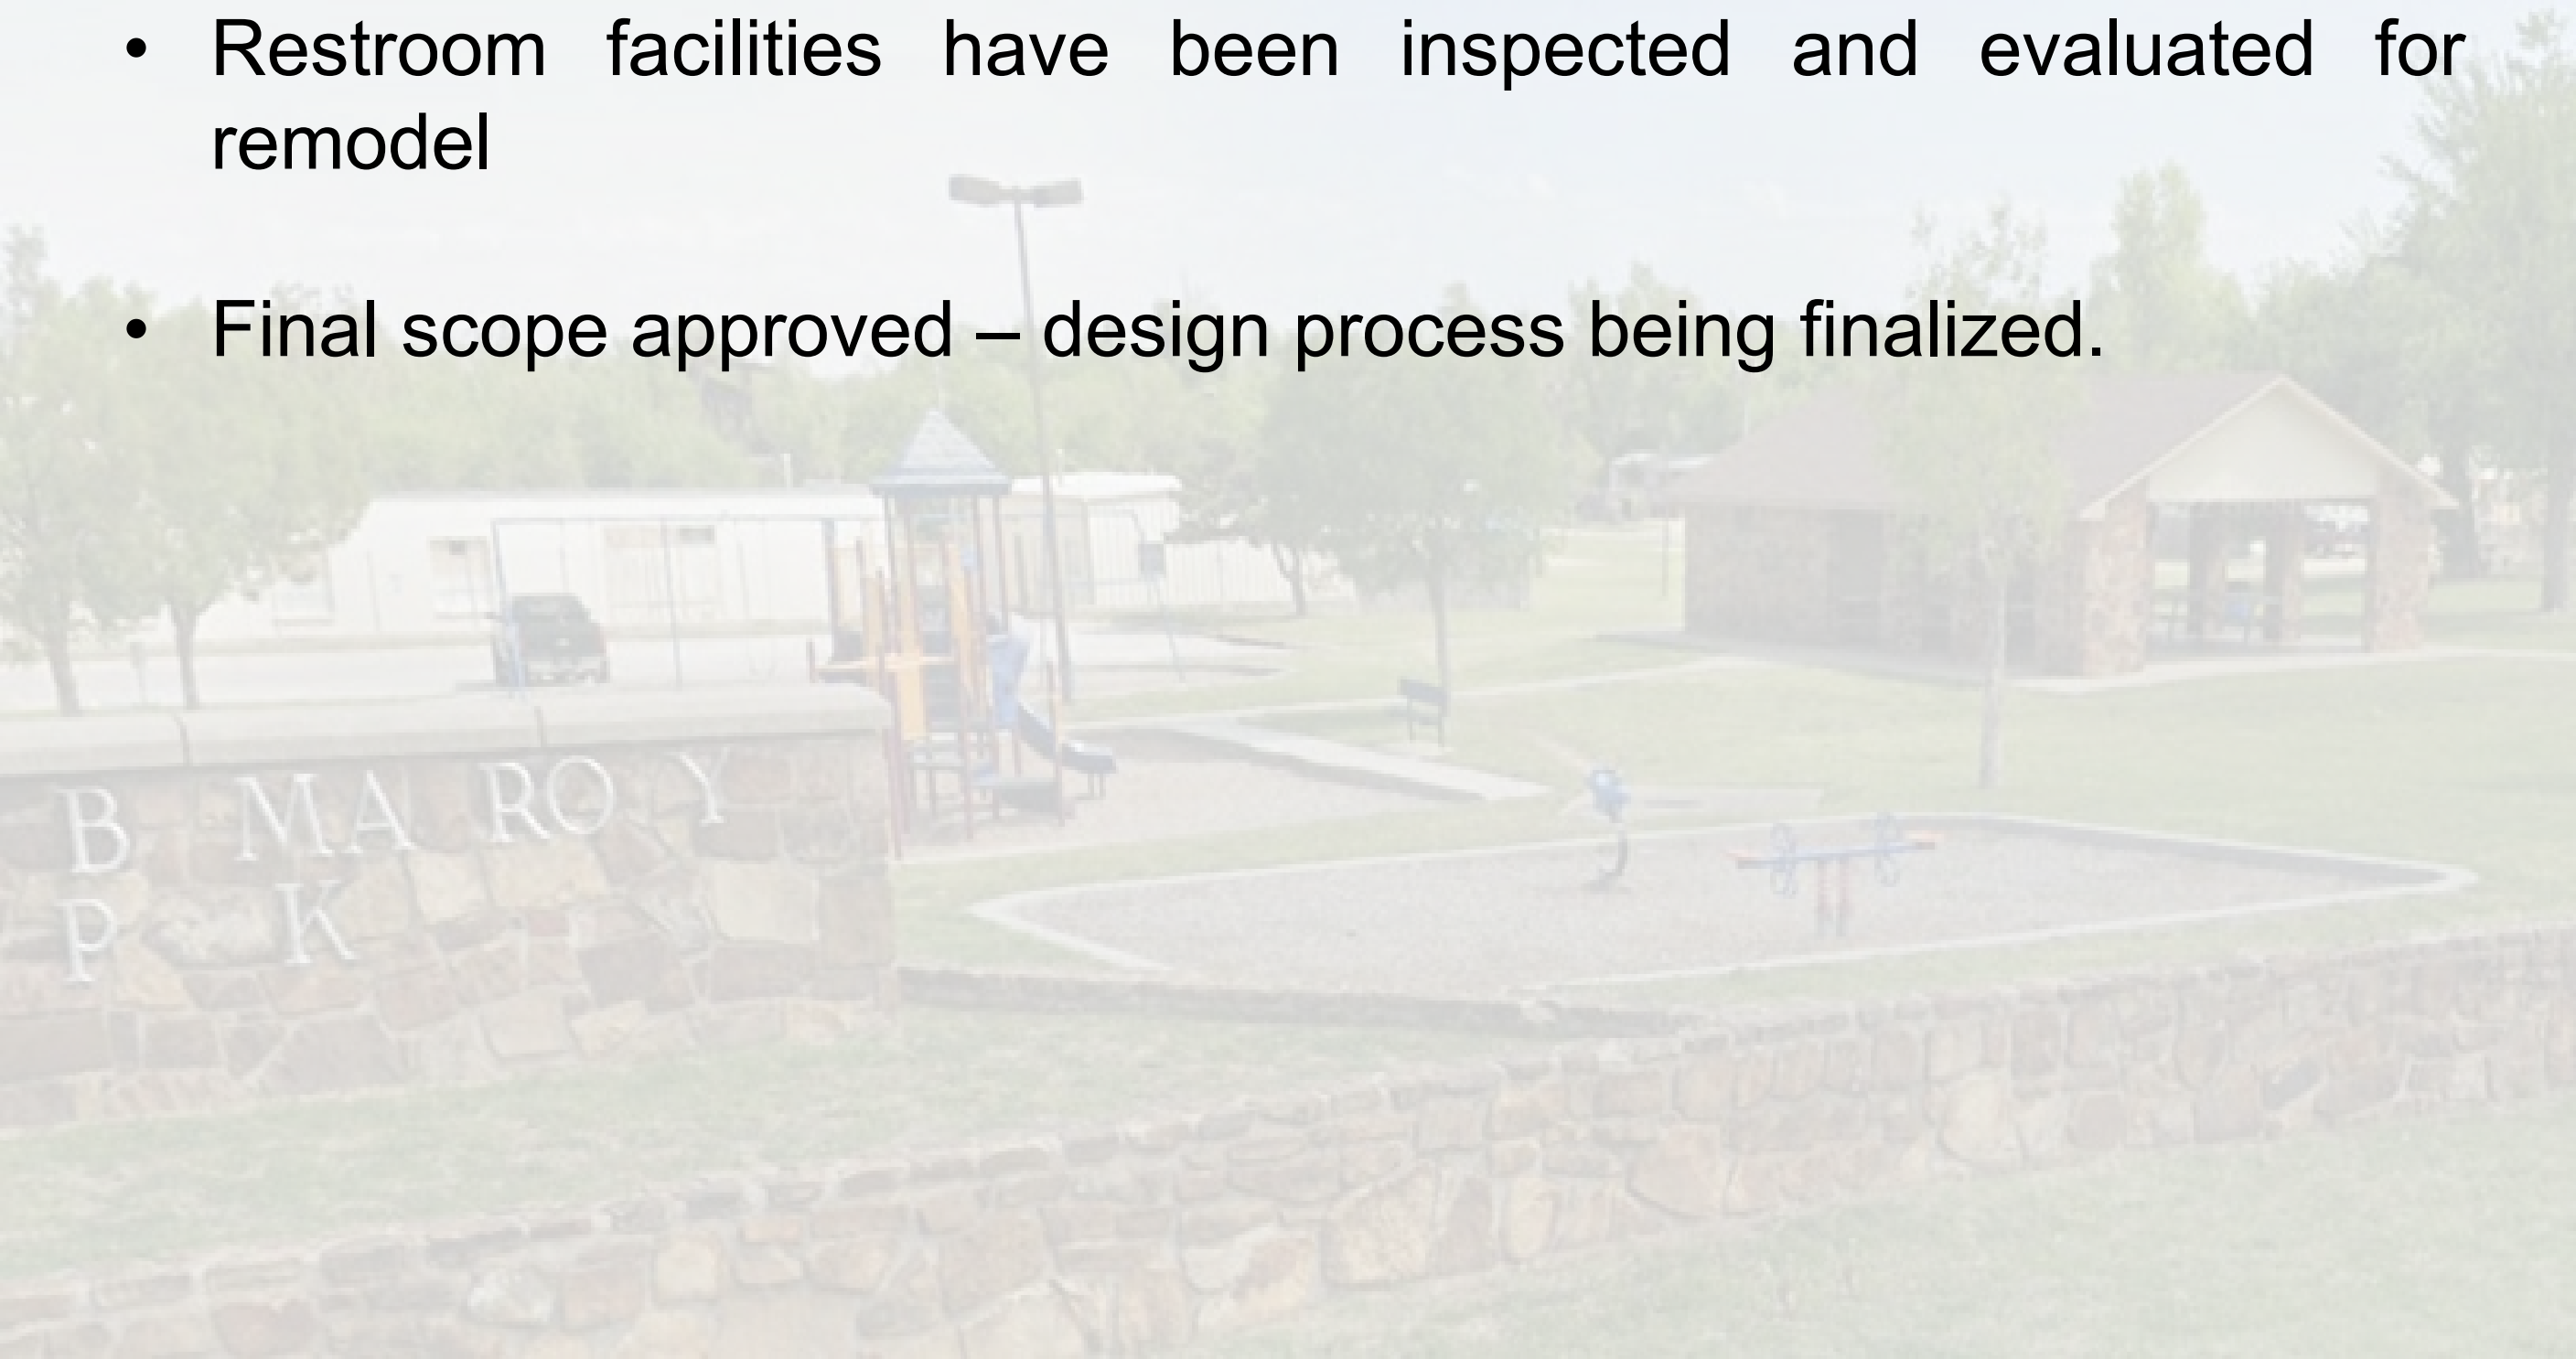

# PROPOSITION 2-E RON CLARK PARK

CITY OF BETHANY



## Acquiring and improving playground and equipping dog park facilities

- Proposed parking lot
- \$40,000 TSET Grant to help fund park improvements



# PROPOSITION 2-F

## CECIL MENDENHALL PARK

CITY OF BETHANY



### Improving but not limited to constructing restroom facilities

- Funding sources to include 2016 G.O. Bond for restroom and fencing improvements
- New restroom location identified
- Evaluating design alternatives



# PROPOSITION 3-A FIRE STATION

CITY OF BETHANY



## Enlarging, remodeling, renovating, equipping and furnishing, but not limited to remodel, renovation, parking lot, sidewalks, architectural and engineering

- Design contract awarded to Troy D. Rhodes and Company
- Construction Management Contract awarded to Lippert Brothers, Inc.
- Design documents received June 27, 2023. Under review

# PROPOSITION 3-B

## POLICE HEADQUARTERS

CITY OF BETHANY



**Enlarging, remodeling, renovating, equipping and furnishing, but not limited to repairing and replacing the existing roof and enlarging, renovating and equipping the evidence room.**

- Geotechnical soil borings - complete
- Footing recommendations - complete
- Survey - complete
- Floor plans, building elevations and roofing designs have been submitted and reviewed by the Police Department – Under design by CH Guernsey

# PROPOSITION 3-C ANIMAL SHELTER

CITY OF BETHANY



## Repairing, renovating, equipping and furnishing the existing animal shelter facility within the City of Bethany located at 5100 North College Avenue

- Geotechnical soil boring - complete
- Footing recommendations - complete
- Survey - complete
- A sanitary sewer has been found that was not shown on any city atlas that is currently under part of the building. Plans to realign the sanitary sewer under design
- Building expansion under design

# PROPOSITION 4-A DRAINAGE

CITY OF BETHANY



**Constructing, improving, enlarging, engineering, equipping, and repairing storm drainage facilities within the City of Bethany. These projects may be completed in phases and funds provided by other governmental agencies and other sources may be used to complete these projects.**

- Identifying project locations and priorities
- Identifying additional funding sources



## American Rescue Plan Act funded Water Meter Replacement Matching \$1,500,000 Grant

- Project approved by OWRB on June 20, 2023, plans advertised for bids
- Pre-bid meeting held June 21, 2023
- Bids were opened on June 29, 2023
- Anticipate award at City Council on July 18, 2023
- Construction anticipated to begin late 2023

# ARPA FUNDED PROJECTS

## SANITARY SEWER REPLACEMENT

CITY OF BETHANY



### American Rescue Plan Act funded Sanitary Sewer Replacement on Peniel, in the amount of \$3,372,692

- Project includes lift station and sanitary sewer line replacement
- Video of existing sewer line underway, with anticipated completion July 31, 2023
- Survey to include areas of failed sewer identified in the video
- Design anticipated to be complete by Winter 2023, and submitted to ODEQ
- Construction contract award anticipated Spring 2024


# ARPA FUNDED PROJECTS

## SANITARY SEWER REPLACEMENT


CITY OF BETHANY



### American Rescue Plan Act funded Sanitary Sewer Replacement on Peniel, in the amount of \$3,372,692

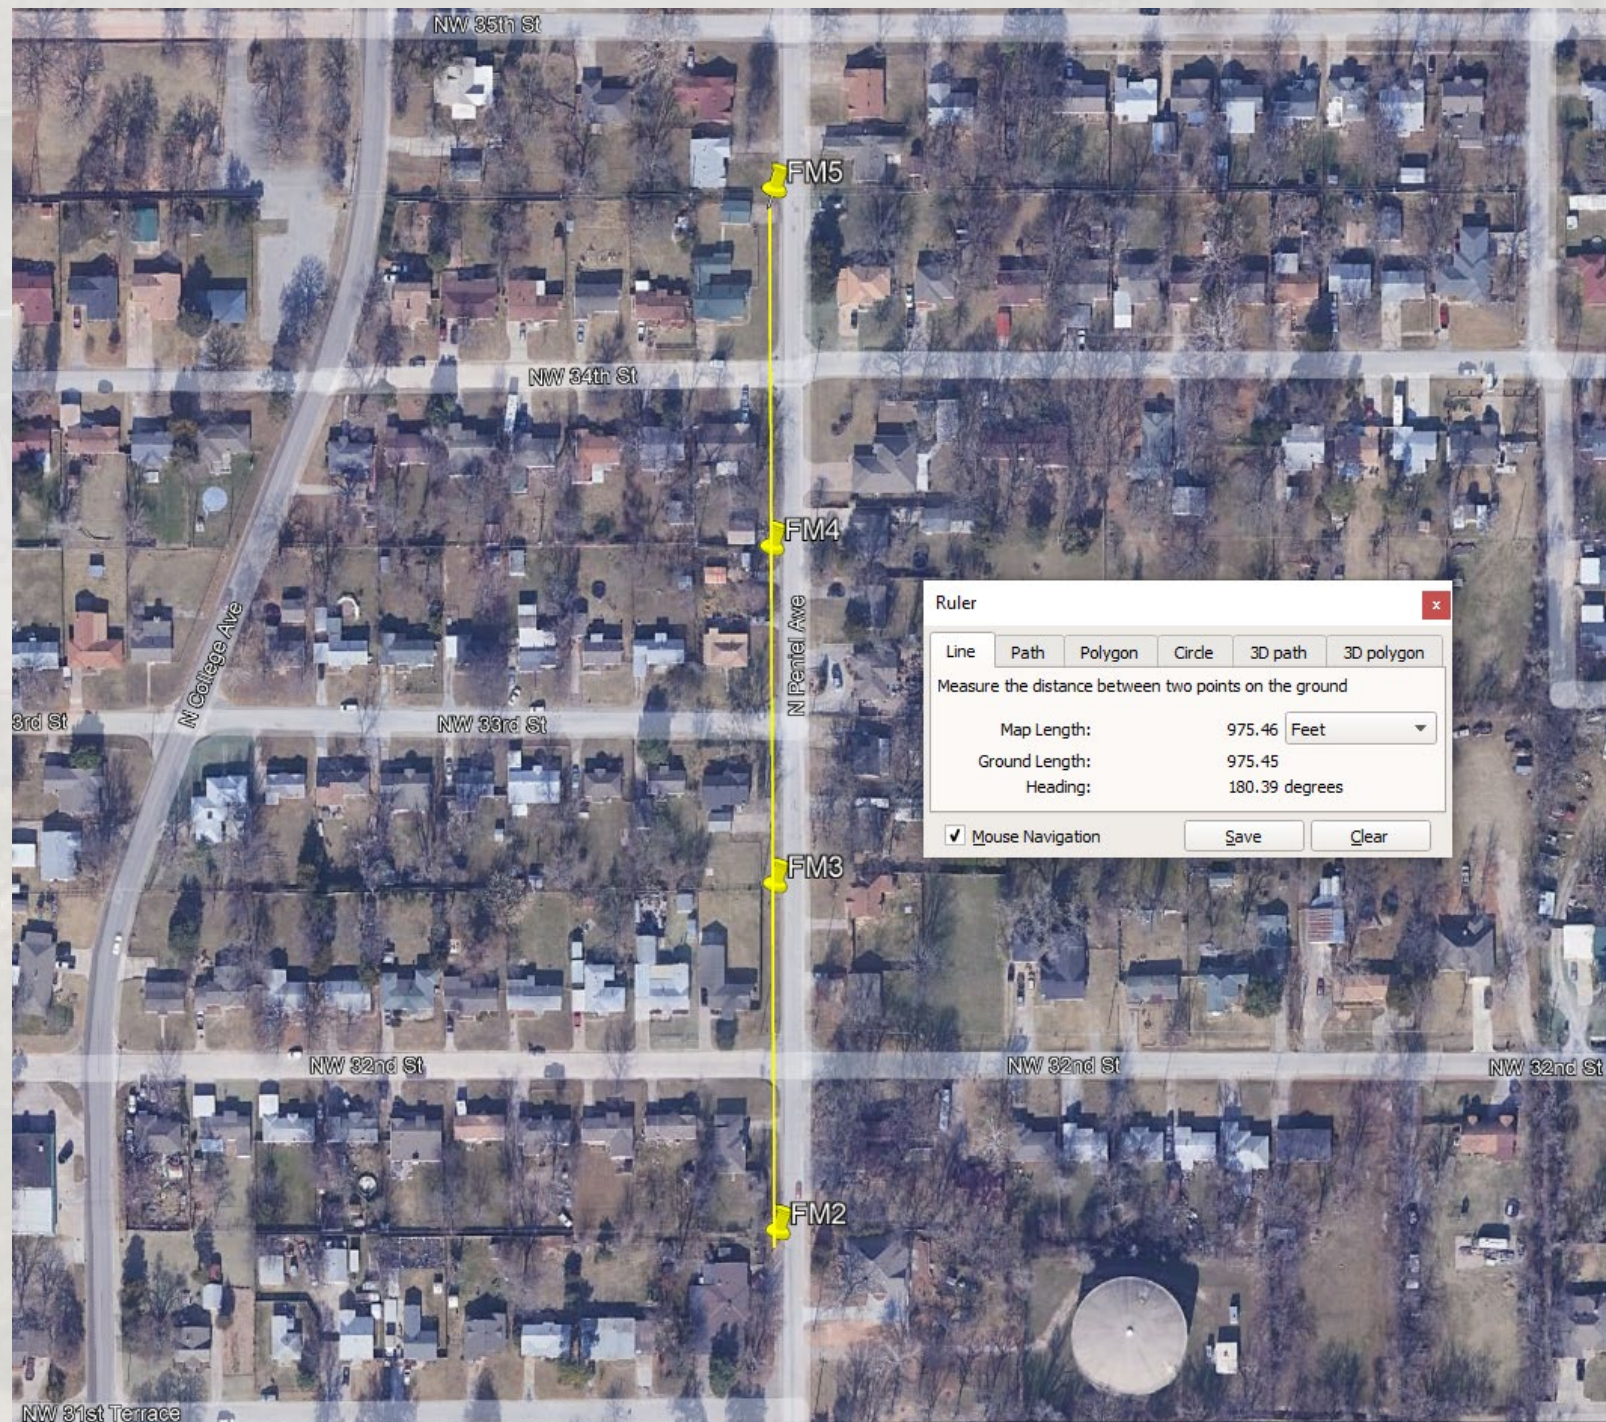

Current video of existing sewer line locations





## American Rescue Plan Act funded Well and Wellfield Improvements in the amount of \$4,600,000

- Survey Complete
- Water Model Complete
- Plans 95% complete
- ODEQ permit application to be submitted upon water lease agreement
- Plans submitted to OWRB upon receipt of ODEQ permit
- Plans anticipated to be submitted to City for permission to advertise Fall 2023
- Construction contract award anticipated Winter 2023



# PROPOSED IMPROVEMENTS TO SH-66

(NW 39<sup>TH</sup> EXPRESSWAY) N. ASBURY AVE. TO N.DONALD AVE.

CITY OF BETHANY



## Proposed Improvements

- Improve Pedestrian Access and Safety, ADA compliant
- Improve Intersection Operations with video detection with new controllers and protected/permissive left turns
- Replace poles with decorative poles
- Improve safety on SH-66 by eliminating on-street parking on north side of SH-66
- Met with members of the downtown association for comments to include in the project
- 90% plans submitted to ODOT
- Utility coordination meeting completed
- Construction contract award anticipated late 2023

