





# CITY OF BETHANY

## OKLAHOMA

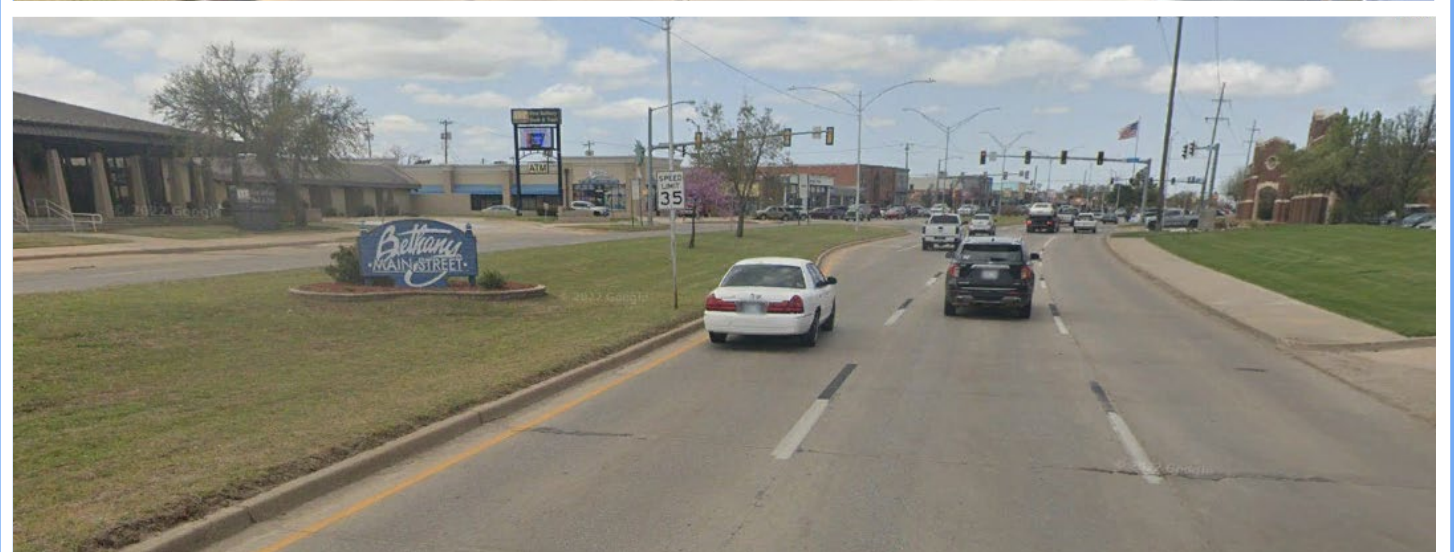

G.O. BOND / ARPA FUNDED PROJECT UPDATES  
ODOT SH-66 PROPOSED IMPROVEMENTS



# PROPOSITION 1-A

## NW 23<sup>RD</sup> STREET / ROCKWELL

CITY OF BETHANY



### Traffic Signalization and Pedestrian Crosswalk Improvements

This project will also include the CRRSAA mill and inlay of the intersection, extending north approximately 1,000 feet.

- Survey complete
- Traffic signal design – TEC - complete
- Roadway mill & inlay design - complete
- ADA ramps and crosswalks design - complete
- CRRSAA project agreement with ODOT approved at June 13<sup>th</sup> City Council Meeting
- Bid let date for signals: December 21, 2023
- Apparent low bidder – Traffic Lighting Systems - \$384,745.14
- Anticipated ODOT bid let date for CRRSAA mill and inlay – Summer 2024

# PROPOSITION 1-B

## NW 36<sup>TH</sup> / ROCKWELL

CITY OF BETHANY



## Traffic Signalization and Pedestrian Crosswalk Improvements

- Survey complete
- Traffic signal design – TEC - complete
- ADA ramps and crosswalks design - complete
- Bid let date for signals: December 21, 2023
- Apparent low bidder – Traffic Lighting Systems - \$434,655.74

# PROPOSITION 1-C

## NW 36<sup>TH</sup> / COUNCIL ROAD

CITY OF BETHANY



## Traffic Signalization and Pedestrian Crosswalk Improvements

- Survey underway
- Evaluating additional funding sources for corridor improvements



# PROPOSITION 1-D

## PENIEL – 39<sup>TH</sup> TO 42<sup>ND</sup>

CITY OF BETHANY



### Peniel Ave. from NW 39<sup>th</sup> Expressway to NW 42<sup>nd</sup> Street

Reconstruction of Peniel Avenue beginning at NW 39<sup>th</sup> Expressway extending north approximately 1,300 feet to NW 42<sup>nd</sup> Street. Reconstruction of Plain Jointed PC Concrete.

- Survey: Complete
- Environmental: Complete
- Roadway Design: Complete. Plan in hand held July 26, 2023. Utilities cleared
- Anticipated Bid Let date: TBD due to possible conflicts with sanitary sewer replacement. Sewer line design underway.

# PROPOSITION 1-E

## NW 30<sup>TH</sup> – ROCKWELL TO PENIEL

CITY OF BETHANY



### NW 30<sup>th</sup> Street from Rockwell Avenue to Peniel Avenue

Reconstruction of NW 30<sup>th</sup> pavement beginning at Rockwell Avenue extending east approximately 2,600 feet to Peniel Avenue. Reconstruction of Plain Jointed PC Concrete.

- Survey: Complete
- Environmental: Complete
- Roadway Design: Complete. Plan in hand held July 26, 2023. Utilities cleared
- Bid Let Date: December 21, 2023
- Apparent low bidder – All Roads Paving Inc. - \$512,822.57

# PROPOSITION 1-F

## MUELLER – NW 44<sup>TH</sup> TO NW 50<sup>TH</sup>


CITY OF BETHANY



### N. Mueller Avenue from NW 44<sup>th</sup> Street to NW 50<sup>th</sup> Street

Reconstruction of Mueller Avenue pavement beginning at NW 44<sup>th</sup> Street extending north approximately 1,960 feet to NW 50<sup>th</sup> Street. Reconstruction of Plain Jointed PC Concrete.

- Survey: Complete
- Environmental: Complete
- Roadway Design: Complete. Plan in hand held July 26, 2023. Utilities cleared. Additional storm sewer inlet locations being identified to assist in removing storm water runoff from Mueller.
- Bid Let Date: December 21, 2023
- Apparent low bidder – All Roads Paving Inc. - \$524,411.60



# PROPOSITION 1-G

## DIVIS – NW 36<sup>TH</sup> TO NW 39<sup>TH</sup>

CITY OF BETHANY



### N. Divis Avenue from NW 36<sup>th</sup> Street to NW 39<sup>th</sup> Expressway

Reconstruction of the west half of Divis Street beginning at NW 36<sup>th</sup> Street extending north approximately 1,960 feet to just south of NW 39<sup>th</sup> Expressway. Reconstruction of Plain Jointed PC Concrete.

- Survey: Complete
- Environmental: Complete
- Roadway Design: Complete. Plan in hand held July 26, 2023. Utilities cleared
- Bid Let Date: December 21, 2023
- Apparent low bidder – All Roads Paving Inc. - \$478,899.28

# PROPOSITION 1-H

## PENIEL – NW 25<sup>TH</sup> TO NW 30<sup>TH</sup>

CITY OF BETHANY



### Peniel Avenue from NW 25<sup>th</sup> Street to NW 30<sup>th</sup> Street

Reconstruction of the west half of Peniel Avenue beginning at NW 25<sup>th</sup> Street extending north approximately 1,955 feet to NW 30<sup>th</sup> Street. Reconstruction of Plain Jointed PC Concrete.

- Survey: Complete
- Environmental: Complete
- Roadway Design: Complete. Plan in hand held July 26, 2023. Utilities cleared.
- Anticipated Bid Let Date: TBD due to possible conflicts with sanitary sewer replacement. Sewer line design underway.

# PROPOSITION 2-A ELDON LYON PARK

CITY OF BETHANY



## Repair, improve, remodel, equip, and renovate playground, exercise station, multipurpose shelters, and remodel restroom facilities.

- Restroom facilities have been inspected and evaluated for remodel.
- Multipurpose shelter concepts presented and recommended for approval by the Parks Board.
- Final scope approved - design process being finalized.

# PROPOSITION 2-B

## RIPPER PARK

CITY OF BETHANY



### Acquiring and improving playground equipment, and constructing or remodeling restroom facilities

- Restroom facilities have been inspected and evaluated for remodel
- Final scope approved – design process being finalized.

# PROPOSITION 2-C

## HENRY GARRISON PARK

CITY OF BETHANY



### Acquiring and improving playground equipment, constructing a multipurpose pavilion, and constructing or remodeling restroom facilities

- Restroom facilities have been inspected and evaluated for remodel
- Multipurpose shelter concepts presented and recommended for approval by the Parks Board
- Final scope approved – design process being finalized.

# PROPOSITION 2-D


## MACRORY PARK

CITY OF BETHANY



### Acquiring and improving playground equipment, and constructing or remodeling restroom facilities

- Restroom facilities have been inspected and evaluated for remodel
- Final scope approved – design process being finalized.

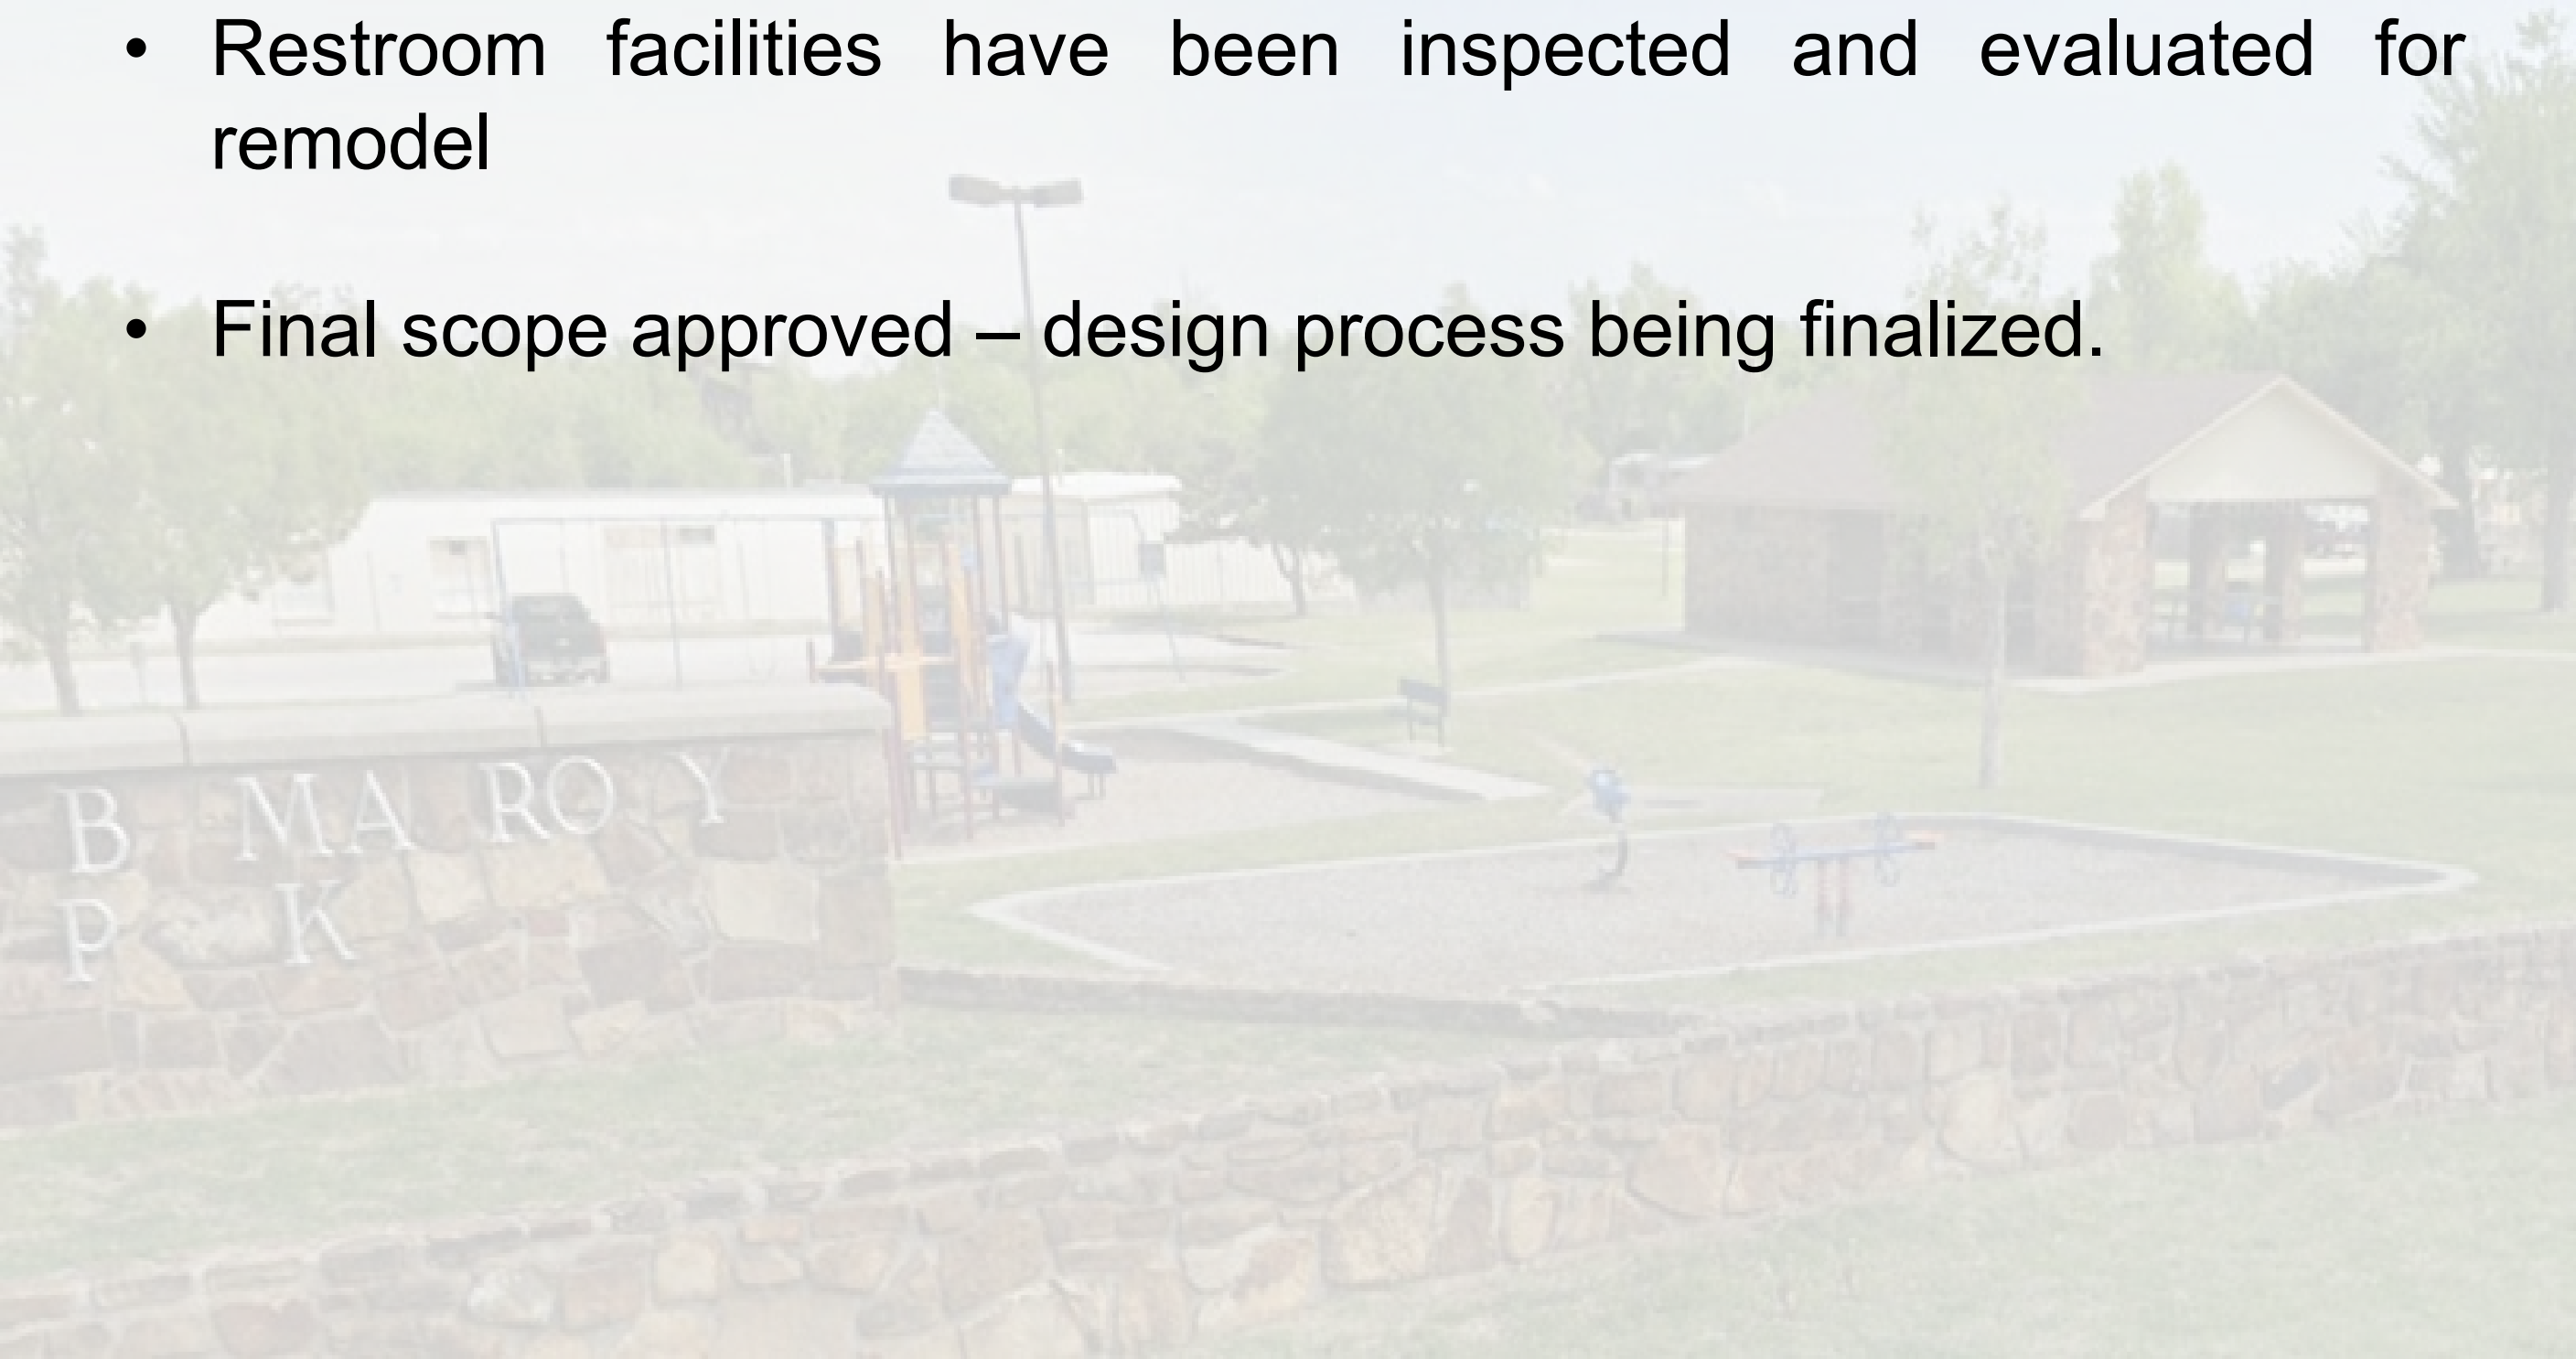



# PROPOSITION 2-F


## CECIL MENDENALL PARK

CITY OF BETHANY



### Improving but not limited to constructing restroom facilities

- Funding sources to include 2016 G.O. Bond for restroom and fencing improvements
- New restroom location identified
- Final design underway




# PROPOSITION 3-A FIRE STATION

CITY OF BETHANY



## Enlarging, remodeling, renovating, equipping and furnishing, but not limited to remodel, renovation, parking lot, sidewalks, architectural and engineering

- Design contract awarded to Troy D. Rhodes and Company
- Construction Management Contract awarded to Lippert Brothers, Inc. - \$1,161,519
- Under construction

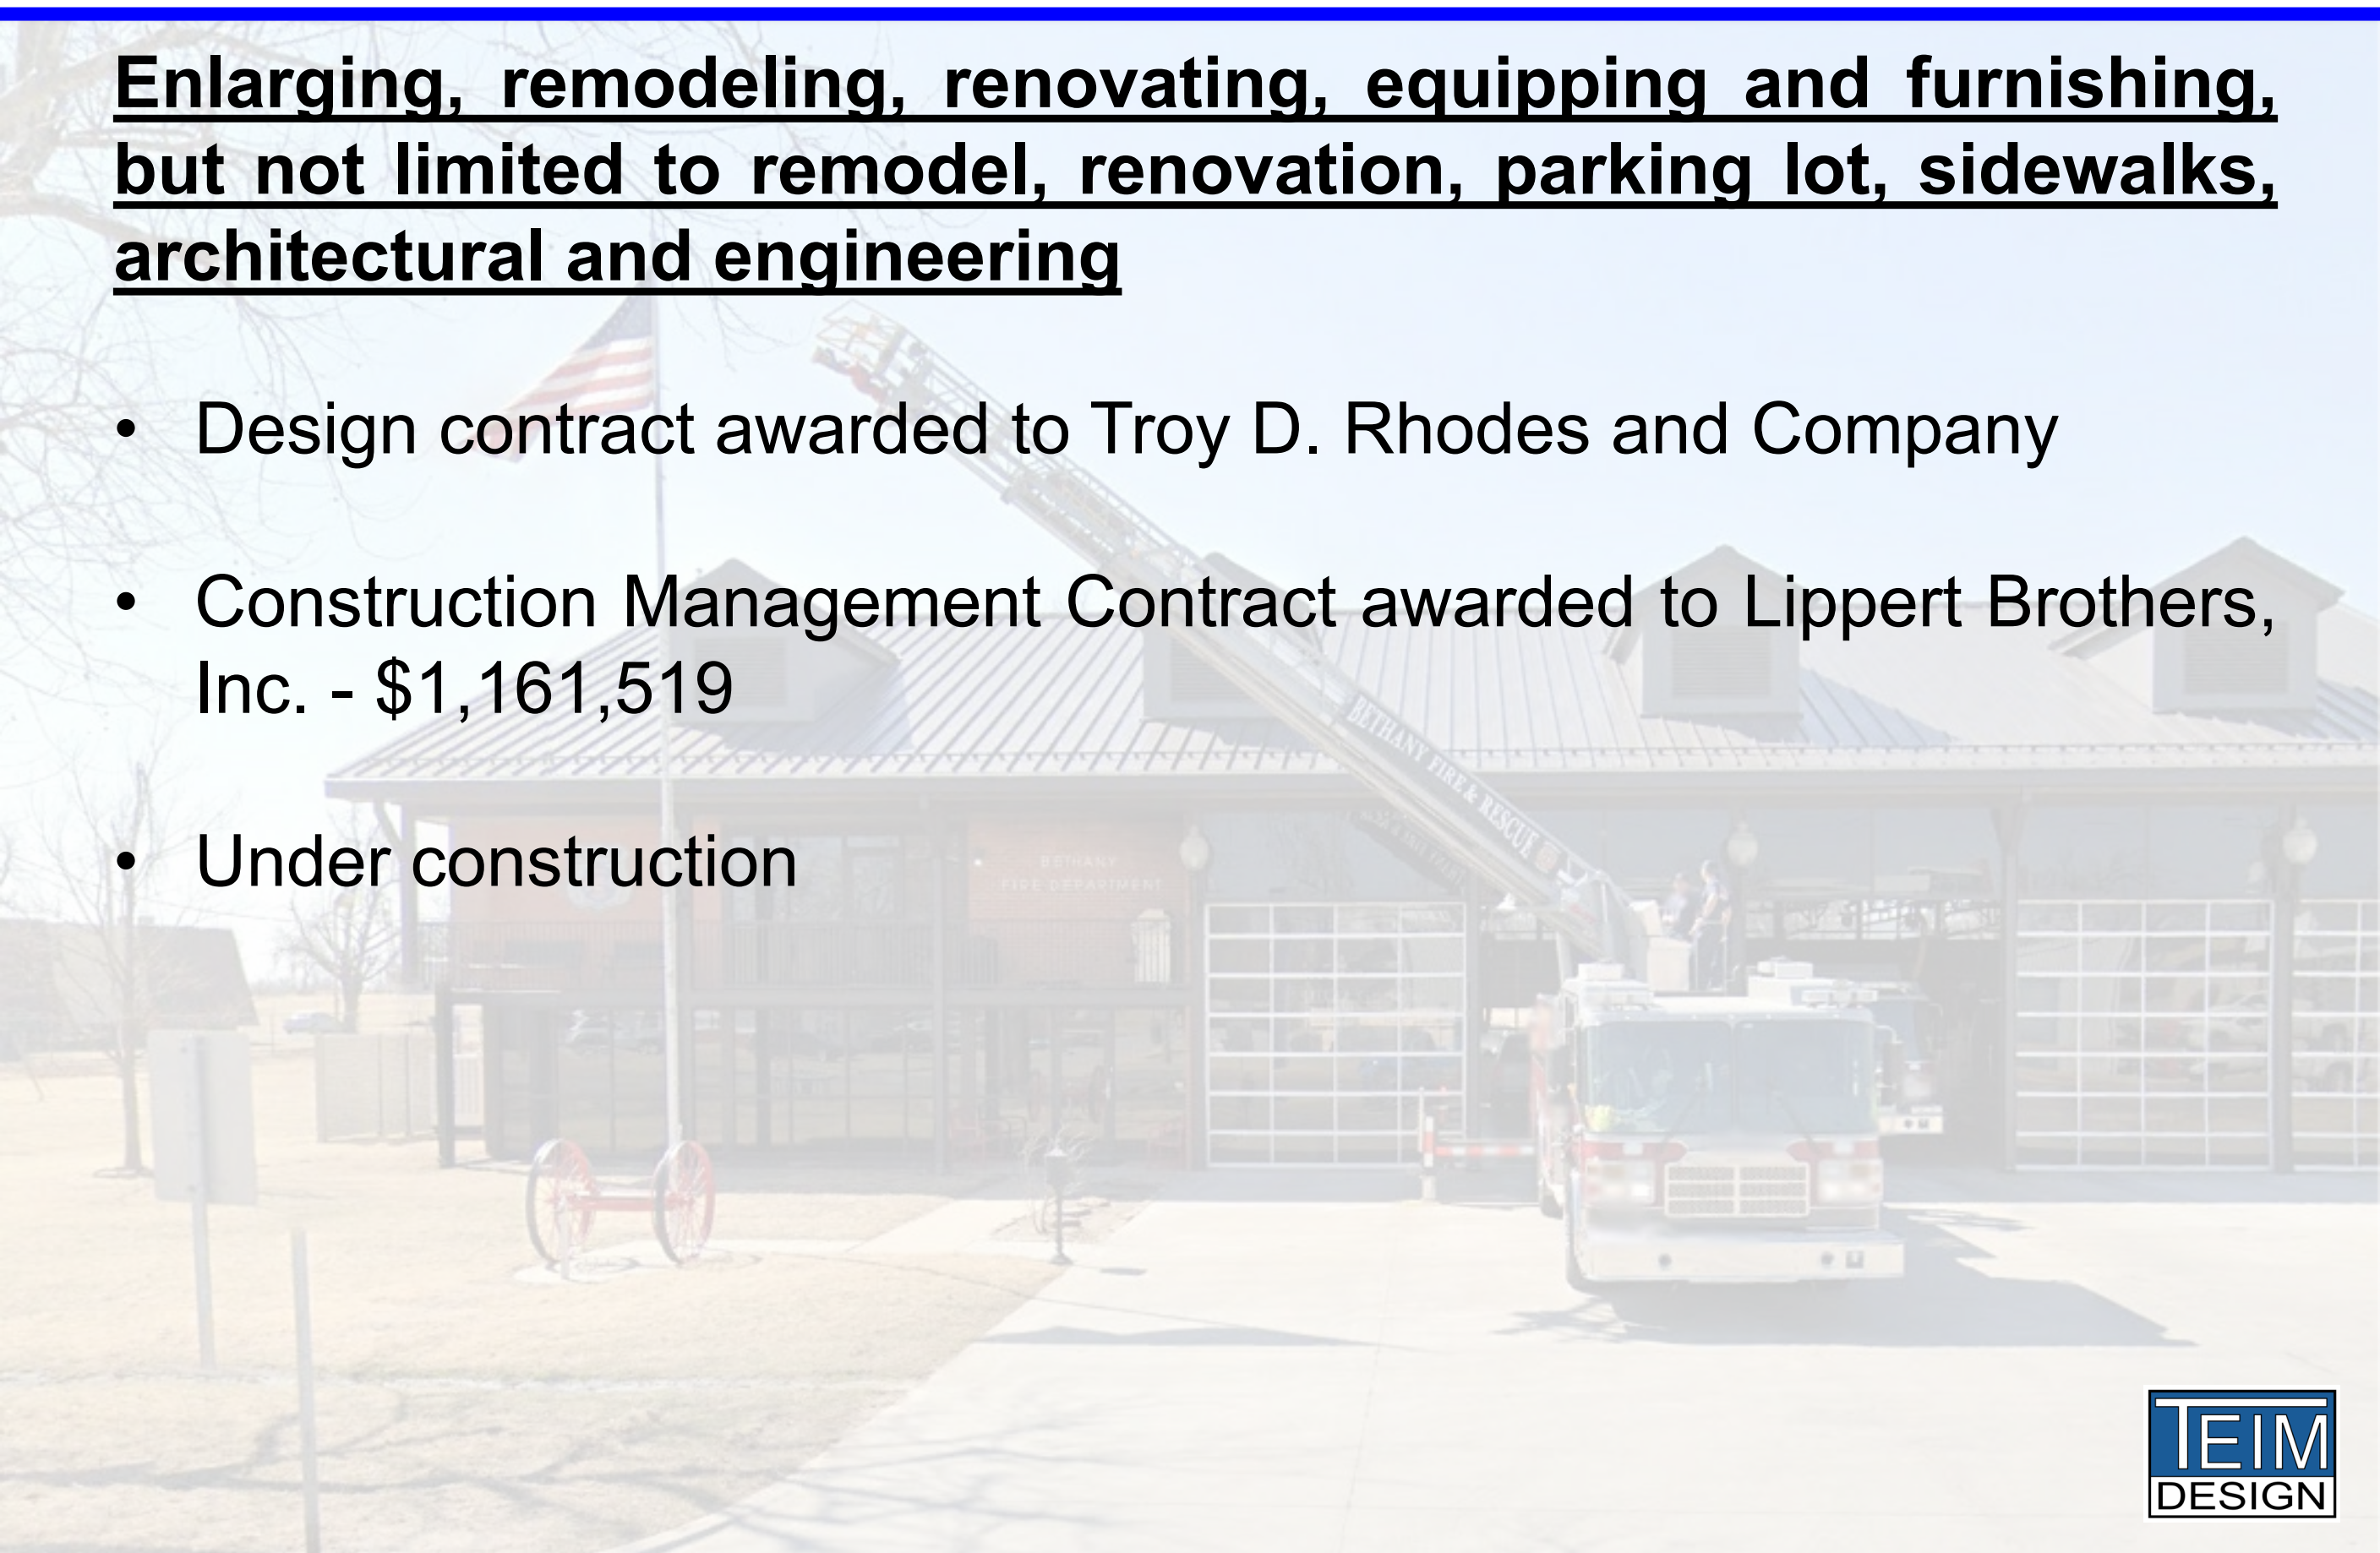

# PROPOSITION 3-B

## POLICE HEADQUARTERS – BUILDING ADDITION

CITY OF BETHANY



**Enlarging, remodeling, renovating, equipping and furnishing, but not limited to repairing and replacing the existing roof and enlarging, renovating and equipping the evidence room.**

- Design complete
- Bids Received: September 12, 2023
- Low Bidder: Holland Construction, LLC. - \$358,800
- Under construction

# PROPOSITION 3-B

## POLICE HEADQUARTERS – ROOF REPLACEMENT

CITY OF BETHANY



**Enlarging, remodeling, renovating, equipping and furnishing, but not limited to repairing and replacing the existing roof and enlarging, renovating and equipping the evidence room.**

- Design complete
- Bids Received: August 30, 2023
- Low Bidder: Heritage Hills Commercial Services, LLC. - \$431,950

# PROPOSITION 3-C

## ANIMAL SHELTER

CITY OF BETHANY



### Repairing, renovating, equipping and furnishing the existing animal shelter facility within the City of Bethany located at 5100 North College Avenue

- Geotechnical soil boring - complete
- Footing recommendations - complete
- Survey - complete
- A sanitary sewer has been found that was not shown on any city atlas that is currently under part of the building. Plans to realign the sanitary sewer are complete and have been approved by the ODEQ.
- Bid Let Date: December 21, 2023
- Apparent low bidder – Luckinbill - \$123,792.00
- Building expansion under design, conceptual drawings have been reviewed by the Police Department and comments are being included in the plans.

# PROPOSITION 4-A DRAINAGE

CITY OF BETHANY



**Constructing, improving, enlarging, engineering, equipping, and repairing storm drainage facilities within the City of Bethany. These projects may be completed in phases and funds provided by other governmental agencies and other sources may be used to complete these projects.**

- Identifying and prioritizing CMP's under pavement
- Identifying additional funding sources



## American Rescue Plan Act funded Water Meter Replacement Matching \$1,500,000 Grant

- Project approved by OWRB on June 20, 2023, plans advertised for bids
- Pre-bid meeting held June 21, 2023
- Bids were opened on June 29, 2023
- Phase 1 bid awarded at City Council on July 18, 2023 to S.W. Water Works in the amount of \$2,544,540.00
- Construction began in October 2023 with anticipated completion in April 2024
- New ultrasonic meters are already being installed with new construction projects in the City.
- Phase 2 County ARPA funded project design complete
- Bid let date January 17, 2024

# ARPA FUNDED PROJECTS

## SANITARY SEWER REPLACEMENT

CITY OF BETHANY



### American Rescue Plan Act funded Sanitary Sewer Replacement on Peniel, in the amount of \$3,372,692

- Project includes lift station and sanitary sewer line replacement
- Video of existing sewer line complete
- Survey is complete
- Design anticipated to be complete by Spring 2024, and submitted to ODEQ
- Construction contract award anticipated Summer 2024

# ARPA WELL & WELLFIELD IMPROVEMENTS

CITY OF BETHANY



- Existing wellfield production 3.01 MGD
- Re-drilling water wells to increase production by 1.1 MGD
- Rehabilitating 8 wells (2, 5, 9, 15, 16, 25, 212, and 213) increases production to 0.3 MGD
- Increase capacity in wellfield transmission lines to transport increased production to the water treatment plant
- Current ARPA funding is \$4.6 million
- Plans complete and received approval from ODEQ
- Plans submitted to OWRB for approval. Pending OWRB approval, anticipated let date February 14, 2024

# PROPOSED IMPROVEMENTS TO SH-66

(NW 39<sup>TH</sup> EXPRESSWAY) N. ASBURY AVE. TO N.DONALD AVE.

CITY OF BETHANY



## Proposed Improvements

- Improve Pedestrian Access and Safety, ADA compliant
- Improve Intersection Operations with video detection with new controllers and protected/permissive left turns
- Replace poles with decorative poles
- Improve safety on SH-66 by eliminating on-street parking on north side of SH-66
- Utility coordination meeting completed
- Plans complete and submitted to ODOT for October letting. Apparent low bidder is SAC Services in the amount of \$2,266,000
- Construction anticipated to begin in early 2024

